

BOSTON WATER & SEWER COMMISSION SOUTH BOSTON SEWER SEPARATION PROJECT Contract No. 21-309-012 CWSRF NO. 7012

MassDEP

Report for June 1 through June 30, 2024

OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission.


The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation-related sites.

CONTRACT 2 UPDATE THROUGH JUNE 30, 2024

Over the month of June, the contractor, working with two crews, completed work at several locations. Completed work includes: water main replacement on Baxter Street from D Steet to E Street; water main replacement on E Street from West Seventh Street to Old Colony Avenue; water bypass removal along project area prior to the 4th of July holiday; and sewer installation at the intersection of Old Colony Avenue and D Street.

ONGOING AND UPCOMING WORK

The contractor will continue with storm drain and sanitary sewer installation on E Street, from West Seventh Street to Old Colony Avenue, and water, storm drain, and sanitary sewer installation on D Street from Old Colony Avenue towards West Seventh Street.

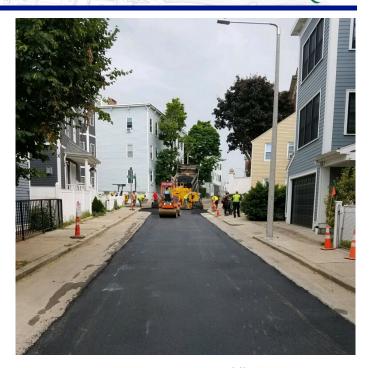

Temporary paving on Middle Street



Sewer Manhole on Old Colony Avenue at D Street



INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS, AND WATER MAINS IN SOUTH BOSTON – CONTRACT 2



Contractor: Fed. Corp., Dedham, Massachusetts Status as of June 30, 2024 Contract No. 21-309-012 CWSRF NO.7012

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	2818 LF	45.26%
10" - 24" Sewer	3492 LF	50.46%
4" – 20" Water Main	7322 LF	62.88%

SCHEDULING SUMMARY

Notice to Proceed: 09/11/2023
Work Commenced: 09/12/2023
Anticipated Completion Date: 04/06/2026

SCHEDULE ASSESSMENT

The contractor has completed 151 of the contracted 400 working days and 62.25% of time remaining.

PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Project Total	14
Other	5
Damage	3
Noise/dust/debris	0
Sewer break/back up	0
Loss/discoloration of water, or low pressure	4
Parking/access	2

PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues 1 **Other Total** 1

SAFETY

Incidents reported this period 0
Incidents reported to-date 0

Contact us at:

Project Field Office Voicemail: 617-865-9299 (daytime) or 617-989-7900 (24/7 emergency)

Email: sbss@bwsc.org
