

# BOSTON WATER & SEWER COMMISSION SOUTH BOSTON SEWER SEPARATION PROJECT Contract No. 21-309-012 CWSRF NO. 7012

CWSRF NO. 7012

Report for May 1 through May 31, 2024



#### **OVERALL PROJECT UPDATE**

The Boston Water and Sewer Commission's South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission.

The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation-related sites.

### **CONTRACT 2 UPDATE THROUGH MAY 31, 2024**


Over the month of May, the contractor completed work at several locations, including: water main, storm drain and sewer replacement and installation on Woodward Street; water main replacement on Sayward Place; water main, sewer and storm drain replacement and installation on Middle Street; rehabilitation of sewer and installation of new storm drain on Tuckerman Street; rehabilitation of sewer on Old Colony Avenue; and water main replacement on Baxter Street from C Street to D Street.

#### ONGOING AND UPCOMING WORK

The contractor will continue with water main, storm drain, and sanitary sewer installation on E Street from West Seventh Street to Old Colony Avenue, and water, storm drain, and sanitary sewer installation on D Street from Old Colony Avenue towards West Seventh Street.



Temporary Paving on Middle Street

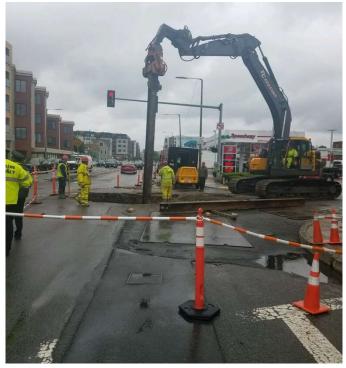

Support of Excavation on D Street



### INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS, AND WATER MAINS IN SOUTH BOSTON – CONTRACT 2



Contractor: Fed. Corp., Dedham, Massachusetts Status as of May 31, 2024 Contract No. 21 309 012 CWSRF NO.7012

### MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	2818 LF	45.26%
10" – 24" Sewer	3340 LF	48.27%
4" – 20" Water Main	5898 LF	50.65%

#### **SCHEDULING SUMMARY**

Notice to Proceed: 09/11/2023 Work Commenced: 09/12/2023 Anticipated Completion Date: 04/06/2026

#### SCHEDULE ASSESSMENT

The contractor has completed 131 of the contracted 400 working days and 67.25% of time remaining.

### PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Project Total	10
Other	4
Damage	1
Noise/dust/debris	1
Sewer break/back up	0
Loss/discoloration of water, or low pressure	2
Parking/access	2

## PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

7.0.1111110	
Parking/access and other issues	1
Other Total	1

#### **SAFETY**

Incidents reported this period	0
Incidents reported to-date	0



Trench on D Street at Old Colony Avenue

Email: sbss@bwsc.org
