



**BOSTON WATER & SEWER COMMISSION  
SOUTH BOSTON SEWER SEPARATION PROJECT**

**Contract No. 21-309-012**

**CWSRF NO. 7012**

**Report for October 1 through October 31, 2024**



## OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission.

The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation-related sites.

## CONTRACT 2 UPDATE THROUGH OCTOBER 31, 2024

Over the month of October, the contractor worked with one crew and completed installation of watermain on West Eighth Street towards E Street, and 12-inch watermain on D Street from West Seventh Street to Old Colony Avenue, and installed watermain connections from D Street at Baxter Street and Bell Court.

## ONGOING AND UPCOMING WORK

The contractor will install new watermain on West Eighth Street from D Street to the north section of West Eighth Street and connect to existing pipeline.



*Hydrant installation on West Eighth Street*



*Trench Excavation for drain install on West Eighth Street*

Contact us at:

Project Field Office Voicemail: 617-865-9299 (daytime) or 617-989-7900 (24/7 emergency)

Email: [sbss@bwsc.org](mailto:sbss@bwsc.org)



# INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS, AND WATER MAINS IN SOUTH BOSTON – CONTRACT 2



Contractor: Fed. Corp., Dedham, Massachusetts  
Status as of October 31, 2024

Contract No. 21-309-012  
CWSRF NO.7012

## MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	3744 LF	60.14%
10" – 24" Sewer	4816 LF	69.60%
4" – 20" Water Main	9121 LF	78.32%

## SCHEDULING SUMMARY

Notice to Proceed:	09/11/2023
Work Commenced:	09/12/2023
Anticipated Completion Date:	04/06/2026

## SCHEDULE ASSESSMENT

The contractor has completed 229 of the contracted 400 working days and 42.75% of time remaining.

## PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Parking/access	2
Loss/discoloration of water, or low pressure	4
Sewer break/back up	0
Noise/dust/debris	0
Damage	4
Other	8


**Project Total 18**

## PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues	1
<b>Other Total</b>	<b>1</b>

## SAFETY

Incidents reported this period	0
<b>Incidents reported to-date</b>	<b>0</b>

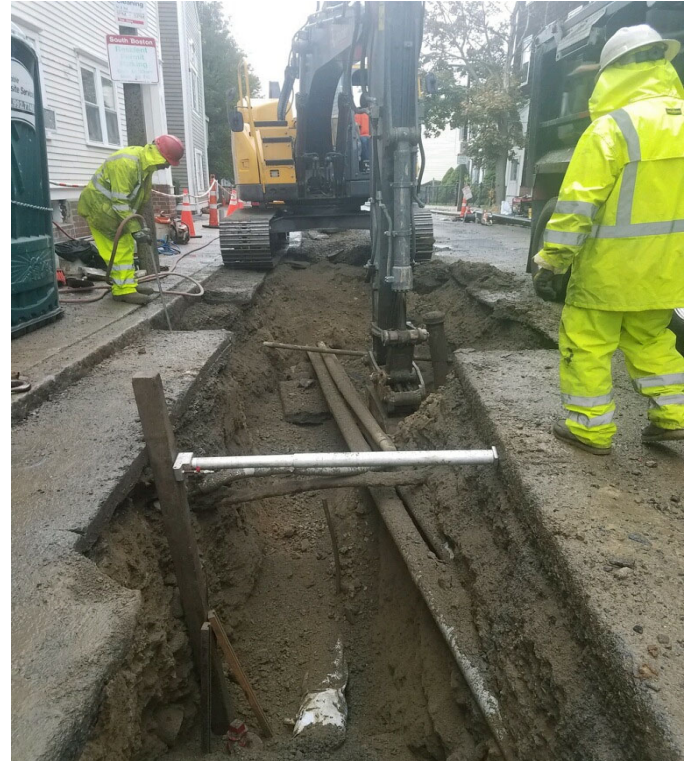

*Trench Excavation of watermain in West Eighth Street*

Contact us at:

Project Field Office Voicemail: 617-865-9299 (daytime) or 617-989-7900 (24/7 emergency)

Email: sbss@bwsc.org
