

November Project Update

CONTRACTOR: Albanese D & S, Dracut, MA
CONTRACT NO. 15-309-011

Work Completed in September & October 2017:


- Mount Pleasant Avenue – Water, Sewer and Drain Relay is complete from Dudley Street to Forest Street
- Forest Place- 2" Water main complete from Forest Street to dead end
- Dudley Street- 24" Sewer relay from Mount Pleasant Place to Vine Street

Upcoming Work in Winter 2017:

- Dudley Street
 - 24" Sewer and 48" Drain installation from Mount Pleasant Place to Hampden Street
 - Tie in of new Sewer and Drains on Adams Street and Vine Street and Mount Pleasant Ave
- Adams Street
 - 12" Drain Installation

Upcoming Work in Spring 2018:

- Dudley Street
 - 24" Sewer and 48" Drain from Hampden Street to Blue Hill Ave
- Blue Hill Avenue
 - Sewer and Drain Installation
- Mount Pleasant Avenue
 - Sewer and Drain from Forest Street To Blue Hill Ave

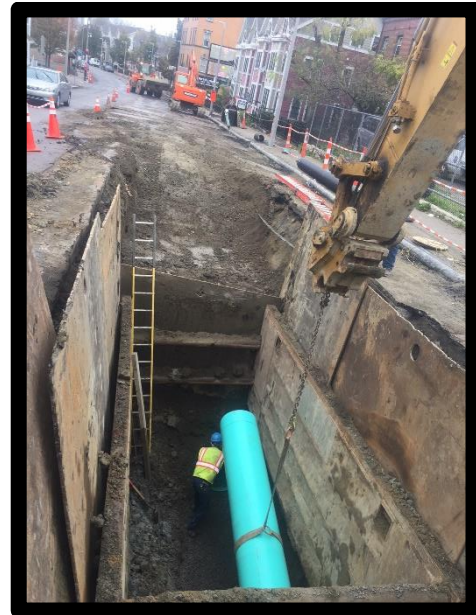

**Dudley Street
Installation of 24" Sewer Pipe**



**Dudley Street
Excavation for 24" Sewer Installation**

Construction Contacts: For additional information contact.

Commission:

Director of Construction:	Irene McSweeney	(617) 989-7447
Project Engineer:	Peter Salvatore	(617) 989-7450
Inspector:	Mike Rivers	(617) 293-2289

Contractor: Albanese D & S

Project Manager:	David Laramee	(617) 593-3733 (c) (978) 937-0909 (o)
------------------	---------------	--

24/7 Emergency:

BWSC: (617) 989-7000

We appreciate your patience and cooperation as we complete this difficult work.

THE FOLLOWING PROVIDES AN UPDATE OF COMPLETED WORK AND WORK REMAINING:

Completed Liner Work

Limits		Date Completed	Scope
Adams Street	Forest Street to Dudley Street	3/22/2017	12" CS
Forest Street	Mount Pleasant Ave. to #16 Forest St.	3/22/2017	12" CS
Forest Street	#16 to #38 Forest St.	3/22/2017	12" CS
Mount Pleasant Avenue	#43 to #61 Mount Pleasant Avenue	3/28/2017	12" CS
Mount Pleasant Avenue	#61 to #76 Mount Pleasant Avenue	5/24/2017	12" CS
Mount Pleasant Avenue	Forest Street to #39 Mt. Pleasant Ave.	5/30/2017	16"x12" CS

Completed Relay Work

Limits		Date Completed	Scope
Forest Street	Mount Pleasant Ave. to Forest Place	5/12/2017	18" D
Forest Street	Forest Place to Vine Street	6/12/2017	15" D
Forest Street	Mount Pleasant Ave. to #38 Vine St.	6/1/2017	10" S
Mount Pleasant Avenue	Dudley Street to Forest Street	6/8/2017	16" W
Mount Pleasant Avenue	Dudley Street to Forest Street	5/12/2017	12" S
Mount Pleasant Avenue	#39 Mt. Pleasant Ave. to #43 Mt. Pleasant Ave.	4/11/2017	12" S
Mount Pleasant Avenue	Dudley Street to Forest Street	6/8/2017	15" D
Mount Pleasant Avenue	Forest Street to #42 Mt. Pleasant Ave.	6/26/2017	12" D
Mount Pleasant Avenue	#85 Mt. Pleasant Ave. to Forest Street	8/30/17	12" D
Mount Pleasant Avenue	#76 Mt. Pleasant Ave. to Forest Street	9/11/17	10" S
Mount Pleasant Avenue	Forest Street to Forest Street	9/8/17	8" W

Water, Drain, Sewer Installation

Remaining Relay Work

Limits		Projected Completion	Scope
Adams Street	Forest Street to Dudley Street	October 2017	12" D
Adams Street	Forest Street to Dudley Street	October 2017	8" W
Adams Street	Forest Street to Dudley Street	October 2017	12" S
Dudley Street	Dudley St. to Magazine St.	May 2018	12" D
Dudley Street	Mount Pleasant Ave. to Blue Hill Ave.	Winter 2018	48" D
Dudley Street	Mount Pleasant Ave. to Blue Hill Ave.	June 2018	24" S
Dudley Street	Mount Pleasant Ave. to #367 Dudley St.	October 2017	24" W
Dudley Street	Mount Pleasant Ave. to Adams Street	October 2017	12" W
Forest Place	Forest Street to End	7/15/17	2" W
Mount Pleasant Avenue	Forest Street to Blue Hill Ave.	January 2017	18" D
Mount Pleasant Avenue	Forest Street to Blue Hill Ave.	January 2017	12" S
